

PLATTE CANYON WATER AND SANITATION DISTRICT

FACILITY OWNERSHIP STATISTICAL REPORT YEAR ENDING DECEMBER 31, 2019

Water

Miles of Water Main Installed in 2019	1.10
No. of Isolation Valves Installed in 2019	35
No. of Blow-off Valves Installed in 2019	0
No. Fire Hydrants Installed in 2019	5
Miles of Water Main in System as of 12/31/2019	77.49
No. of Isolation Valves in system as of 12/31/2019	1,217
No. of Blow-off Valves in System as of 12/31/2019	132
No. of Fire Hydrants in System as of 12/31/2019	492

Sewer

Miles of Sewer Main Installed in 2019	0.06
Miles of Sewer Main in System as of 12/31/2019	239.23
No. of Manholes as of 12/31/2019	1,895
No. of Cleanouts as of 12/31/2019	11

FACILITY OWNERSHIP STATISTICAL REPORT

YEAR ENDING DECEMBER 31, 2019

WATER FACILITIES

<u>Size</u>	<u>Type</u>	<u>Total</u> <u>12/31/2018</u>	<u>Add</u>	<u>Subtract</u>	<u>Total</u> <u>12/31/2019</u>
PIPE:					
4"	ACP	1,342			1,342
4"	CIP	3,053			3,053
4"	PVC	3,140	948		4,088
6"	ACP	122,487			122,487
6"	CIP	29,302		1,741	27,561
6"	DIP	875			875
6"	PVC	35,068			35,068
8"	ACP	56,254		1,286	54,968
8"	CIP	18,425		2,791	15,634
8"	DIP	8,753			8,753
8"	PVC	57,314	4,880		62,194
10"	ACP	740			740
10"	CIP	684			684
10"	DIP	253			253
12"	ACP	37,061			37,061
12"	CIP	6,178			6,178
12"	DIP	3,748			3,748
12"	PVC	4,041			4,041
16"	CIP	1,691			1,691
16"	DIP	7,067			7,067
16"	PVC	1,082			1,082
16"	STL	2,217			2,217
18"	STL	8,351			8,351
20"	DIP	12			12
	TOTAL	409,138	5,828	5,818	409,148

ACP: Asbestos Cement Pipe
PVC: Polyvinyl Chloride Pipe
CIP: Cast Iron Pipe
DIP: Ductile Iron Pipe
STL: Steel Pipe

FACILITY OWNERSHIP STATISTICAL REPORT

YEAR ENDING DECEMBER 31, 2019

WATER FACILITIES(continued)

<u>Size</u>	<u>Type</u>	<u>Total</u> <u>12/31/2018</u>	<u>Add</u>	<u>Subtract</u>	<u>Total</u> <u>12/31/2019</u>
VALVES:					
2"	PRV	1			1
4"	Gate	25			25
4"	PRV	3			3
6"	Gate	497	10	20	487
6"	PRV	3			3
8"	Gate	477	25	10	492
8"	PRV	1			1
10"	Gate	11		1	10
10"	PRV	3			3
12"	Gate	179			179
16"	Gate	1			1
16"	Butterfly	7			7
16"	Check	1			1
18"	Butterfly	4			4
	TOTAL	1,213	35	31	1,217
BLOW-OFFS:					
2"	Ball	75			75
2"	Gate	57			57
	TOTAL	1552	0	0	132
HYDRANTS:					
6"	Mueller Cent.	127		1	126
6"	Mueller Im.	53		4	49
6"	Waterous	302	5		307
6"	Amer. Darling	5			5
6"	Kennedy	5			5
	TOTAL	492	5	5	492

FACILITY OWNERSHIP STATISTICAL REPORT

YEAR ENDING DECEMBER 31, 2019

SEWER FACILITIES

<u>Size</u>	<u>Type</u>	<u>Total</u> <u>12/31/2018</u>	<u>Add</u>	<u>Subtract</u>	<u>Total</u> <u>12/31/2019</u>
PIPE:					
6"	VCP	150			150
8"	CP	465			465
8"	VCP	320,251			320,251
8"	PVC	551,391			551,391
8"	C-900	147,480			147,480
8"	CPP	31,970			31,970
8"	CIP	223			223
8"	DIP	84			84
8"	SVC	2,574			2,574
10"	VCP	22,591			22,591
10"	PVC	17,290			17,290
10"	CPP	4,307			4,307
10"	C-900	4,982			4,982
12"	VCP	20,743			20,743
12"	PVC	10,980			10,980
12"	CP	178			178
12"	C-900	1,656			1,656
12"	CPP	2,220			2,220
15"	PVC	12,816	293		13,109
15"	VCP	6,972			6,972
15"	CP	433			433
15"	CPP	14,338			14,338
16"	PEP	1,039		293	746
16"	SRC	2,698			2,698
18"	CPP	6,129			6,129
18"	PEP	4,928			4,928
18"	VCP	9,464			9,464
18"	PVC	1,799			1,799
21"	CPP	4,242			4,242
21"	VCP	3,019			3,019
21"	PVC	6,038			6,038
22"	PEP	4,195			4,195
24"	PEP	3,712			3,712
24"	PVC	203			203
24"	CPP	4,007			4,007
27"	CPP	2,183			2,183
30"	CPE	186			186
33"	CPP	12,821			12,821
36"	CPP	9,503			9,503
42"	CPP	2,816			2,816
42"	SPE	1,616			1,616
45"	CPP	318			318
48"	CPP	6,708			6,708
60"	CPP	1,411			1,411
	TOTAL	1,263,129	293	293	1,263,129

CP: Concrete Pipe
 VCP: Vitriified Clay Pipe
 PVC: Polyvinyl Chloride Pipe
 C-900: Polyvinyl Chloride Pipe C-900 Class 200
 CPP: Cured In-place Pipe

PEP: Polyethylene Pipe
 CIP: Cast Iron Pipe
 DIP: Ductile Iron Pipe
 RCP: Reinforced Concrete Pipe

PLATTE CANYON WATER AND SANITATION DISTRICT

WATER & SEWER SUPPLY REPORT YEAR ENDING DECEMBER 31, 2019

Taps

Water Taps Sold in 2019	4
3/4" Equivalent Water Taps Sold in 2019	4
Sewer Taps Sold in 2019	6
Single Family Equivalent Sewer Taps Sold in 2019	6

Consumption

Total Water Delivered (gallons)	797,885,000
---------------------------------	-------------

WATER & SEWER SUPPLY REPORT - (2010-2019)

	<u>2019</u>	<u>2018</u>	<u>2017</u>	<u>2016</u>	<u>2015</u>	<u>2014</u>	<u>2013</u>	<u>2012</u>	<u>2011</u>	<u>2010</u>
SEWER TAPS:										
Total Active Taps	6,844.00	6,838.00	6,829.00	6,827.00	6,827.00	6,824.00	6,818.00	6,808.00	6,805.00	6,804.00
Single Family Residential	5,812.00	5,806.00	5,797.00	5,796.00	5,796.00	5,793.00	5,789.00	5,782.00	5,779.00	5,778.00
Multi Family Residential	913.00	913.00	913.00	913.00	913.00	913.00	913.00	913.00	913.00	913.00
Commercial	119.00	119.00	119.00	118.00	118.00	118.00	116.00	113.00	113.00	113.00
Taps Sold	6.00	9.00	2.00	0.00	3.00	6.00	10.00	3.00	1.00	2.00
Single Family Residential	6.00	9.00	1.00	0.00	3.00	4.00	7.00	3.00	1.00	0.00
Multi Family Residential	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Commercial	0.00	0.00	1.00	0.00	0.00	2.00	3.00	0.00	0.00	2.00
Total Single Family Equiv.	7,316.87	7,310.87	7,301.87	7,299.87	7,299.87	7,296.87	7,290.87	7,250.87	7,247.87	7,246.87
Single Family Residential	5,801.00	5,795.00	5,786.00	5,785.00	5,785.00	5,782.00	5,778.00	5,771.00	5,768.00	5,767.00
Multi Family Residential	913.00	913.00	913.00	913.00	913.00	913.00	913.00	913.00	913.00	913.00
Commercial	602.87	602.87	602.87	601.87	601.87	601.87	599.87	566.87	566.87	566.87
Single Family Equiv. Sold	6.00	9.00	2.00	0.00	3.00	6.00	40.00	3.00	1.00	6.64
Single Family Residential	6.00	9.00	1.00	0.00	3.00	4.00	7.00	3.00	1.00	0.00
Multi Family Residential	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00	0.00
Commercial	0.00	0.00	1.00	0.00	0.00	2.00	33.00	0.00	0.00	6.64
CONSUMPTION:										
Total Water Delivered*	797,885.00	859,815.00	848,648.00	863,376.00	786,955.00	782,242.00	831,457.00	1,064,104.00	917,049.00	1,039,335.00
Gal./3/4" Equivilant/Day	327.93	353.38	348.85	354.90	323.58	321.69	342.09	438.20	377.81	428.19
Gal./Capita/Day	111.92	120.72	119.32	121.41	110.67	110.06	117.05	149.97	129.30	146.57
Gal./Account/Day	371.64	400.49	395.35	402.21	366.67	364.54	387.67	496.65	428.24	485.34
Single Family Res. - Delivered*	691,921.00	745,418.00	713,707.00	742,053.00	673,120.00	639,311.00	684,710.00	875,935.00	757,473.00	856,792.00
Gal./3/4" Equivilant/Day	325.55	350.72	335.86	349.20	316.87	301.00	322.54	413.05	357.37	404.23
Gal./Account/Day	337.43	363.52	348.11	361.94	328.38	311.94	334.27	428.08	370.39	418.95
Mulit-Family Res. - Delivered*	29,936.00	41,555.00	26,615.00	31,369.00	50,821.00	54,527.00	57,565.00	70,011.00	55,835.00	61,502.00
Gal./3/4" Equivilant/Day	209.76	291.17	186.49	219.80	356.10	382.07	403.36	490.57	391.23	430.94
Gal./Account/Day	543.16	753.97	482.90	569.16	922.09	989.33	1,044.45	1,270.27	1,013.06	1,115.88
Commercial - Delivered*	76,028.00	72,842.00	108,326.00	89,954.00	63,014.00	88,404.00	89,182.00	118,158.00	103,741.00	121,041.00
Gal./3/4" Equivilant/Day	460.83	441.52	656.60	545.24	381.95	535.85	540.56	716.20	628.81	733.67
Gal./Account/Day	1,843.33	1,766.08	2,626.40	2,180.97	1,527.80	2,143.39	2,162.25	2,864.78	2,515.24	2,934.68

*in thousands of gallons


WATER & SEWER SUPPLY REPORT - (2010-2019)

FACILITY:	<u>2019</u>	<u>2018</u>	<u>2017</u>	<u>2016</u>	<u>2015</u>	<u>2014</u>	<u>2013</u>	<u>2012</u>	<u>2011</u>	<u>2010</u>
Water										
Distribution Mains*	77.49	77.49	77.47	77.47	77.47	77.47	77.37	77.37	77.33	77.05
Insatllted (new)**	10.27	79.00	0.00	0.00	0.00	561.00	0.00	198.00	1,492.00	0.00
Installed (replaced)**	5,817.73	3,208.00	149.00	0.00	1,120.00	0.00	0.00	1,425.00	1,045.00	1,491.00
No. Water Main Breaks	11	21	10	7	13	8	9	9	11	4
Valves Op. & Serv.	1,180	1,186	1,191	1,190	1,190	1,187	1,169	1,180	1,179	1,175
Distribution Main Flushing	199	199	194	197	161	159	29	159	158	159
Hydrants Op. Serv.	491	491	463	491	491	491	490	490	490	489
Sewer										
Collection Mains	229.03	228.98	228.98	228.98	228.74	228.74	228.63	228.63	228.63	228.63
Installed (new)**	293.00	0.00	0.00	1,233.00	0.00	609.00	0.00	0.00	0.00	0.00
Installed (replaced)**	0.00	12,621.00	2,969.00	0.00	0.00	0.00	0.00	200.00	300.00	0.00
Interceptor Mains*	10.20	5.82	5.82	5.82	5.82	5.82	5.82	5.82	5.82	5.82
No. Sewer Backups	0.00	1.00	0.00	1.00	1.00	0.00	0.00	0.00	0.00	0.00
Main Televised**	77,009	101,240.00	102,785.00	120,282.00	80,391.00	97,123.00	110,365.00	103,517.00	70,560.00	102,037.00
Main Hyd. Cleaned**	78,338	102,227.00	48,674.00	31,751.00	41,023.00	53,422.00	36,586.00	36,240.00	39,287.00	48,847.00
Main Root Cut**	44,974.00	40,371.00	63,506.00	73,002.00	50,151.00	50,768.00	80,586.00	82,924.00	91,467.00	86,615.00
Main Root Treated**	14,529.00	16,166.00	13,353.00	20,851.00	12,578.00	14,058.00	14,797.00	9,851.00	0.00	0.00
ADMINISTRATION:										
No. Full Time Equivalent	12.12	12.26	12.08	11.97	10.94	11.34	10.73	10.66	10.79	11.02
Total Hours Worked	25,208.16	25,495.00	25,136.00	24,891.00	22,745.00	23,590.00	22,324.00	22,170.00	22444	22913.15
Total Hours Worked(PC)	9,839.48	10,808.00	9,935.00	9,156.00	8,569.00	9,213.00	9,021.00	9,404.00	9096	9287.62
Administration	5,942.92	6,306.00	5,347.00	4,746.00	4,115.00	5,189.00	4,704.00	4,874.00	4,786.00	4,742.68
Maintenance	3,896.56	4,502.00	4,588.00	4,410.00	4,454.00	4,024.00	4,317.00	4,530.00	4,310.00	4,544.94
Total Hours Worked(SWM)	13,191.18	12,294.00	12,681.00	12,941.00	12,085.00	12,419.00	11,707.00	11,012.00	11,746.00	11,658.03
Administration	5,824.41	5,615.00	5,359.00	6,113.00	4,470.00	6,071.00	4,967.00	4,869.00	4,939.00	5,206.28
Maintenance	7,366.77	6,679.00	7,322.00	6,828.00	7,615.00	6,348.00	6,740.00	6,143.00	6,807.00	6,451.75
Total Hours Worked(Others)	2,177.50	2,393.00	2,520.00	2,794.00	2,091.00	1,958.00	1,596.00	1,754.00	1,602.00	1,967.50
Administration	834.75	871.00	1,201.00	1,047.00	1,255.00	617.00	423.00	300.00	282.00	358.00
Maintenance	1,342.75	1,522.00	1,319.00	1,747.00	836.00	1,341.00	1,173.00	1,454.00	1,320.00	1,609.50

* miles
 ** feet

PLATTE CANYON W&S DISTRICT


Water Pipe Installed By Year

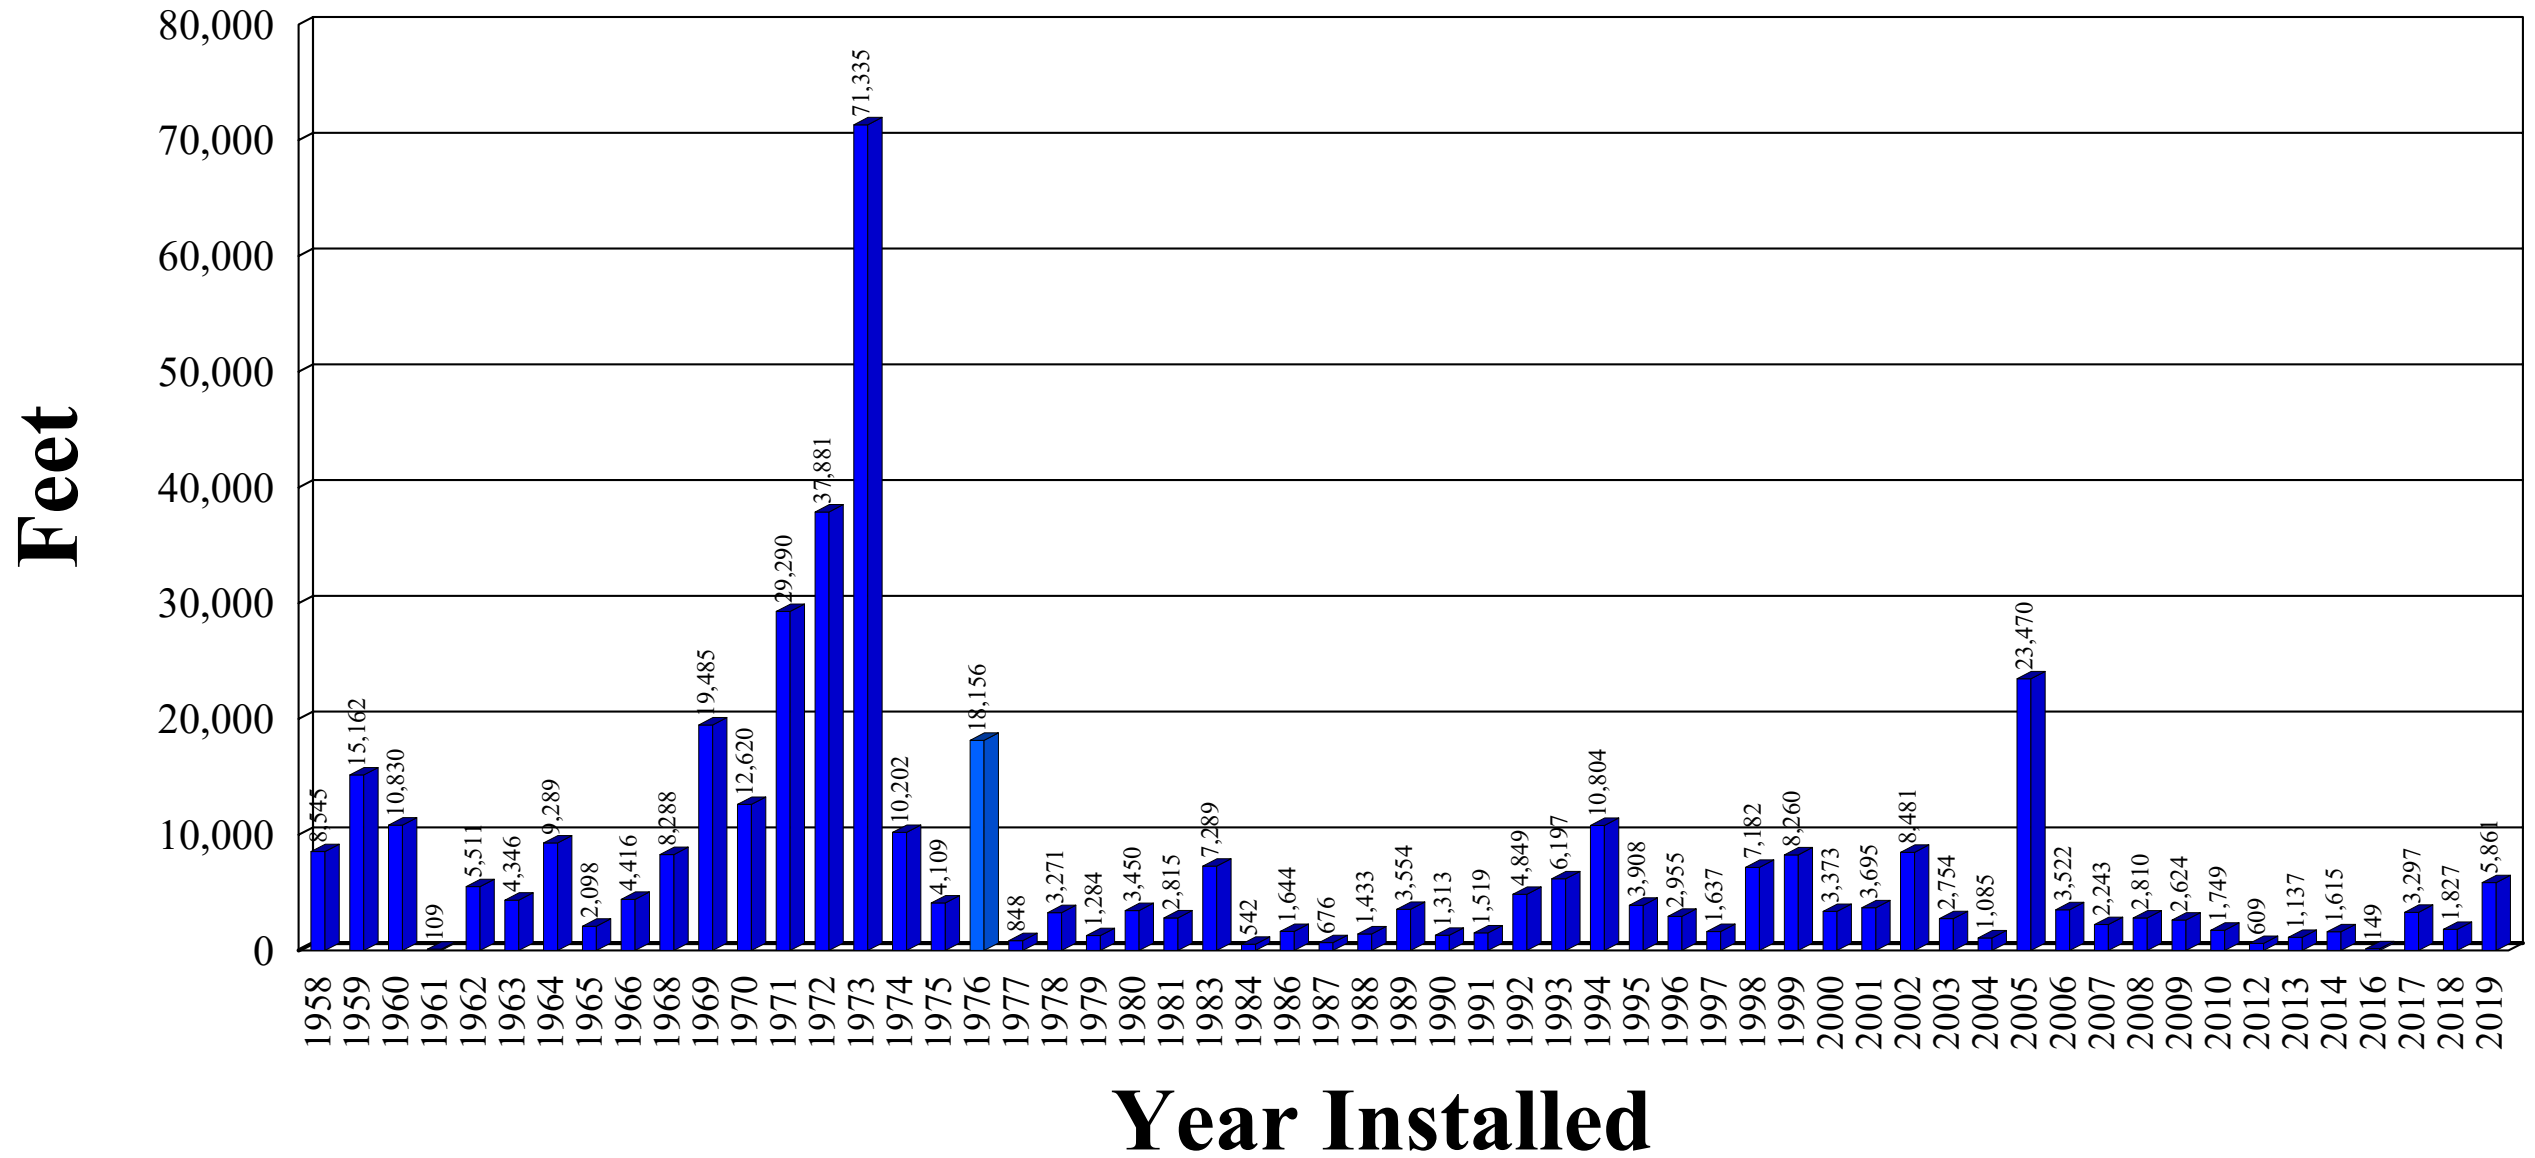

	4			6				8				10			12				16				18		Total
	ASBESTOS CEMENT PIPE	CAST IRON PIPE	POLYVINYL CHLORIDE PIPE	ASBESTOS CEMENT PIPE	CAST IRON PIPE	DUCTILE IRON PIPE	POLYVINYL CHLORIDE PIPE	ASBESTOS CEMENT PIPE	CAST IRON PIPE	DUCTILE IRON PIPE	POLYVINYL CHLORIDE PIPE	ASBESTOS CEMENT PIPE	CAST IRON PIPE	DUCTILE IRON PIPE	ASBESTOS CEMENT PIPE	CAST IRON PIPE	DUCTILE IRON PIPE	POLYVINYL CHLORIDE PIPE	CAST IRON PIPE	DUCTILE IRON PIPE	POLYVINYL CHLORIDE PIPE	STEEL PIPE	DUCTILE IRON PIPE	STEEL PIPE	
2000	0	0	368	0	0	391	41	0	0	0	1,594	0	0	0	0	0	0	0	0	979	0	0	0	0	3,373
2001	0	0	0	0	0	379	1,211	0	0	0	2,104	0	0	0	0	0	0	0	0	0	0	0	0	0	3,695
2002	0	0	0	0	0	330	1,701	0	0	0	6,449	0	0	0	0	0	0	0	0	0	0	0	0	0	8,481
2003	0	0	259	0	0	264	0	0	0	0	2,232	0	0	0	0	0	0	0	0	0	0	0	0	0	2,754
2004	0	0	0	0	0	270	815	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1,085
2005	0	0	2,477	0	0	681	3,917	0	0	30	14,999	0	0	0	0	0	0	0	0	1,366	0	0	0	0	23,470
2006	0	0	269	0	0	57	1,508	0	0	0	606	0	0	0	0	0	0	0	0	0	1,082	0	0	0	3,522
2007	0	0	0	0	0	109	1,368	0	0	0	766	0	0	0	0	0	0	0	0	0	0	0	0	0	2,243
2008	0	0	0	0	0	51	2,079	0	0	0	680	0	0	0	0	0	0	0	0	0	0	0	0	0	2,810
2009	0	0	0	0	0	70	564	0	0	0	1,421	0	0	0	0	0	0	569	0	0	0	0	0	0	2,624
2010	0	0	354	0	0	105	1,289	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1,749
2012	0	0	0	0	0	47	562	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	609
2013	0	0	361	0	0	16	0	0	0	0	760	0	0	0	0	0	0	0	0	0	0	0	0	0	1,137
2014	0	0	0	0	0	43	1,520	0	0	0	52	0	0	0	0	0	0	0	0	0	0	0	0	0	1,615
2016	0	0	0	0	0	0	149	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	149
2017	0	0	0	0	0	55	2,959	0	0	0	5	0	0	0	0	0	112	0	0	155	0	0	12	0	3,297
2018	0	0	0	0	0	25	1,611	0	0	0	0	0	0	0	0	0	191	0	0	0	0	0	0	0	1,827
2019	0	0	0	0	0	32	948	0	0	0	4,881	0	0	0	0	0	0	0	0	0	0	0	0	0	5,861
Total	1,342	3,053	4,088	122,558	27,561	9,052	35,068	54,969	15,635	8,753	62,194	740	684	253	37,061	6,178	3,748	4,042	1,691	7,068	1,082	2,217	12	8,351	417,402

PLATTE CANYON W&S DISTRICT

Sewer Pipe Installed By Year

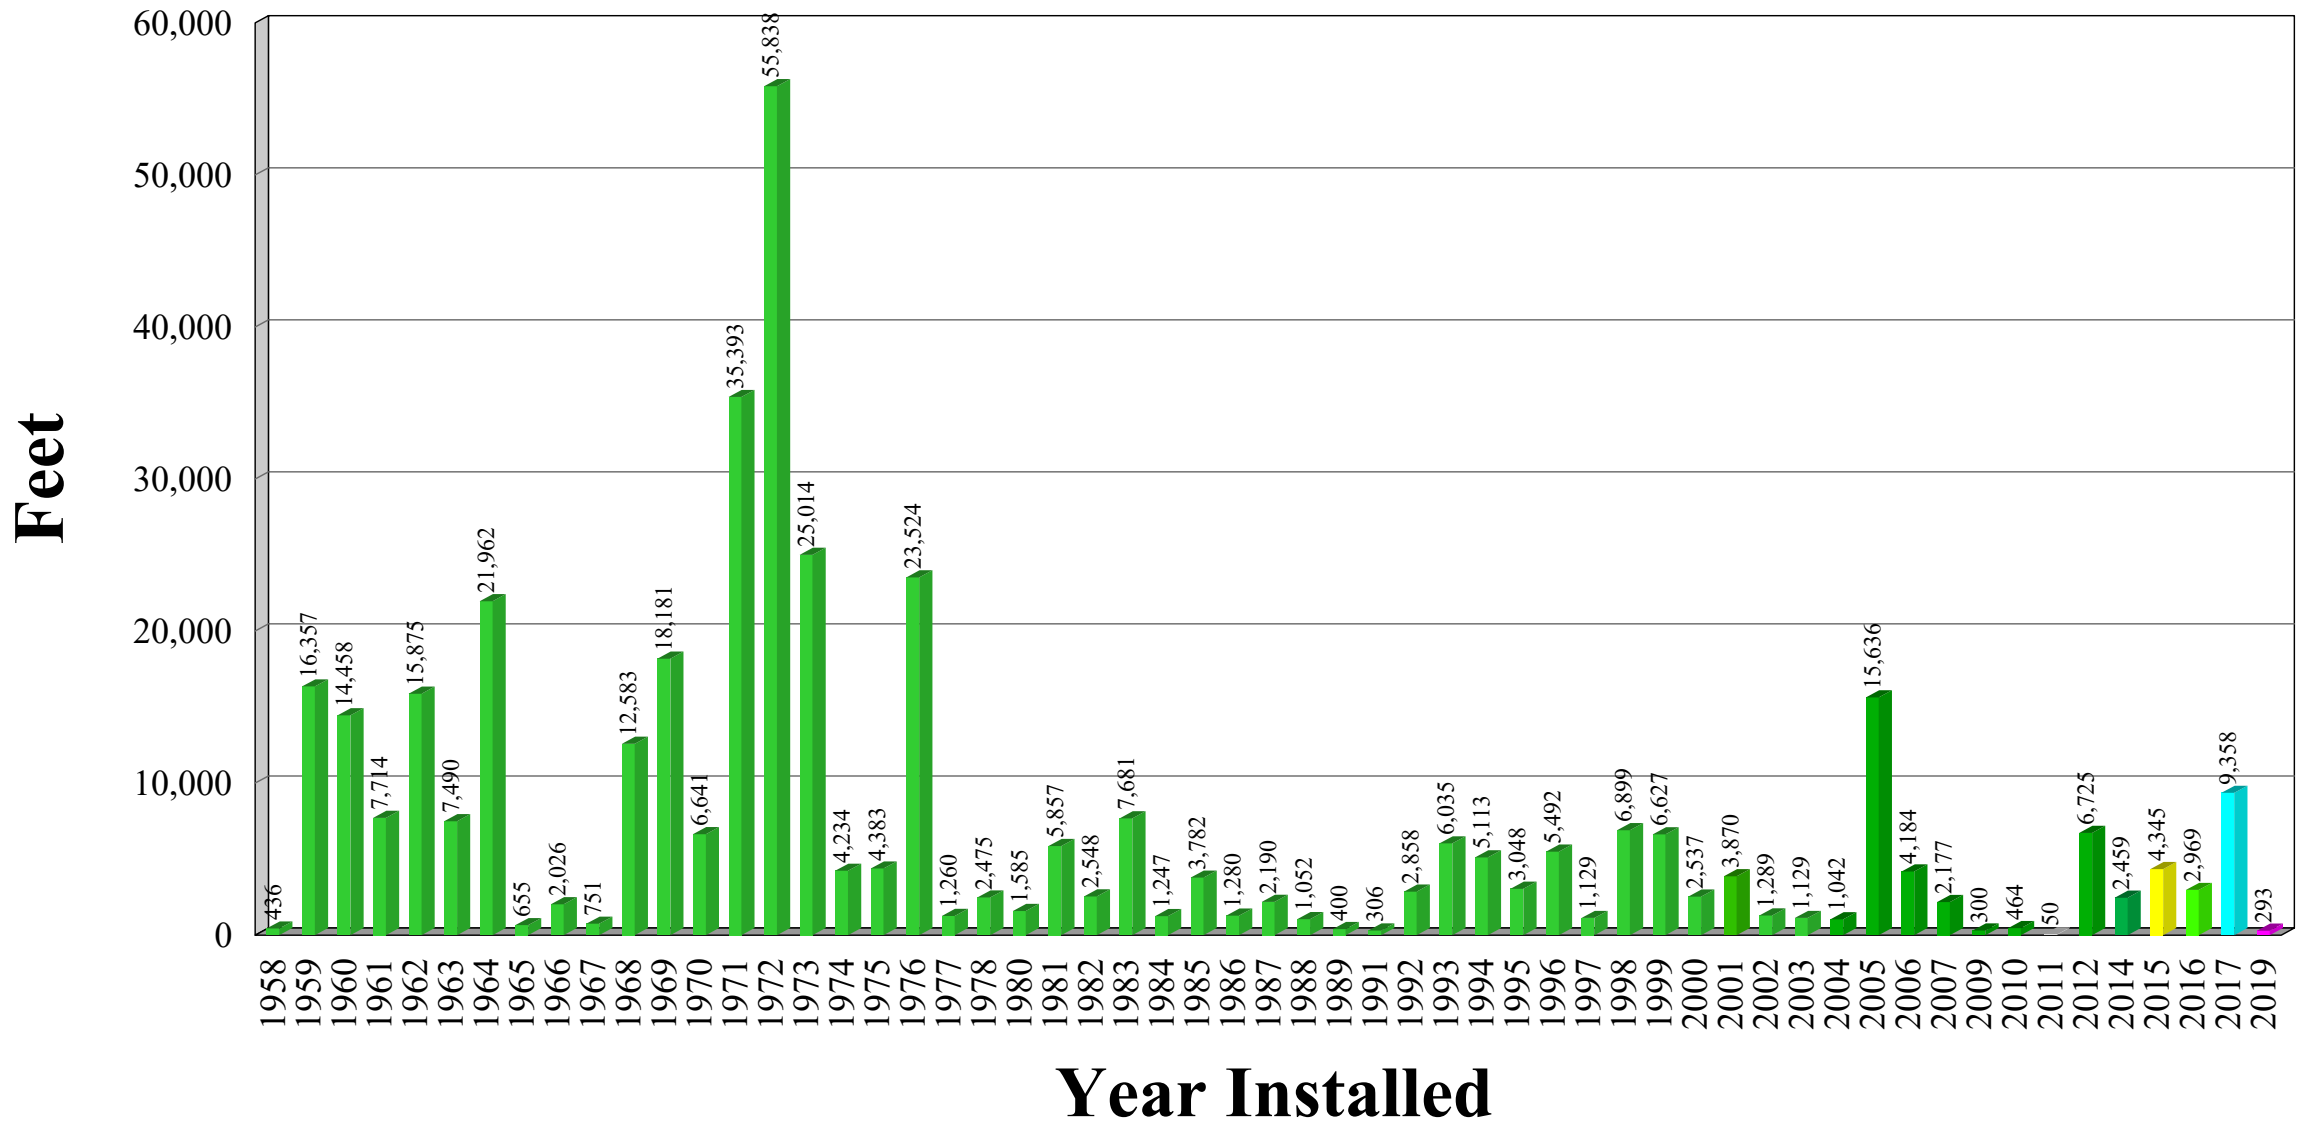

Sewer Pipe Installed By Year

	6		8						10			12		15		16			18		21	22	24			30	Total		
	Vitrified Clay Pipe	C-900 POLYVINYL CHLORIDE PIPE	CAST IRON PIPE	Concrete Pipe (non-reinforced)	CURED IN PLACE PIPE	Ductile Iron Pipe	Polyvinyl Chloride	SLIPLINED VITRIFIED CLAY PIPE	Vitrified Clay Pipe	CURED IN PLACE PIPE	Polyvinyl Chloride	Vitrified Clay Pipe	CURED IN PLACE PIPE	Vitrified Clay Pipe	Concrete Pipe (non-reinforced)	Polyvinyl Chloride	POLYETHYLENE PIPE	Polyvinyl Chloride	SLIPLINED REINFORCED CONCRETE PIPE	CURED IN PLACE PIPE	SLIPLINED REINFORCED CONCRETE PIPE	CURED IN PLACE PIPE	SLIPLINED REINFORCED CONCRETE PIPE	CURED IN PLACE PIPE	Polyvinyl Chloride	SLIPLINED REINFORCED CONCRETE PIPE		CURED IN PLACE PIPE	SPRILITE POLYETHYLENE PIPE
1958	0	0	0	0	0	0	0	0	436	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	436
1959	0	0	0	215	0	0	0	0	15,992	0	0	150	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	16,357
1960	150	0	0	0	0	0	0	0	12,305	0	0	1,460	0	543	0	0	0	0	0	0	0	0	0	0	0	0	0	0	14,458
1961	0	0	0	0	0	0	0	0	4,566	0	0	2,741	0	407	0	0	0	0	0	0	0	0	0	0	0	0	0	0	7,714
1962	0	0	0	0	0	0	0	0	15,169	0	0	706	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	15,875
1963	0	0	0	0	0	0	0	0	7,490	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	7,490
1964	0	0	0	0	0	0	0	0	20,106	0	0	1,856	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	21,962
1965	0	0	0	0	0	0	0	0	655	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	655
1966	0	0	0	0	0	0	0	0	2,026	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	2,026
1967	0	0	0	0	0	0	0	0	751	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	751
1968	0	0	0	0	0	0	0	0	12,583	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	12,583
1969	0	0	0	0	0	0	0	0	14,596	0	0	3,585	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	18,181
1970	0	0	0	0	0	0	0	0	6,341	0	0	300	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	6,641
1971	0	0	0	0	0	0	0	0	32,242	0	0	3,151	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	35,393
1972	0	0	0	0	0	0	295	0	52,834	0	0	2,709	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	55,838
1973	0	0	0	0	0	0	12,651	0	11,479	0	0	884	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	25,014
1974	0	0	0	0	0	0	0	0	4,234	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	4,234
1975	0	0	0	0	0	0	0	0	4,383	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	4,383
1976	0	0	0	0	0	0	11,739	0	9,852	0	1,933	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	23,524
1977	0	0	0	0	0	0	1,260	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1,260
1978	0	0	0	0	0	0	2,475	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	2,475
1980	0	0	0	0	0	0	914	0	0	0	671	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1,585
1981	0	0	223	0	0	0	4,197	0	165	0	0	0	0	0	200	1,072	0	0	0	0	0	0	0	0	0	0	0	0	5,857
1982	0	0	0	0	0	0	2,548	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	2,548
1983	0	0	0	0	0	0	4,817	2,574	290	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	7,681
1984	0	0	0	0	0	0	1,247	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	1,247
1985	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	526	0	2,205	0	1,051	0	0	0	0	0	3,782
1986	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	0	631	0	649	0	0	0	0	0	1,280

	6	8							10			12		15		16			18		21	22	24			30	Total	
	Victorized Clay Pipe	C-900 POLYVINYL CHLORIDE PIPE	CAST IRON PIPE	Concrete Pipe (non-reinforced)	CURED IN PLACE PIPE	Ductile Iron Pipe	Polyvinyl Chloride	SLIPLINED REINFORCED VITRIFIED CLAY PIPE	Victorized Clay Pipe	CURED IN PLACE PIPE	Polyvinyl Chloride	Victorized Clay Pipe	CURED IN PLACE PIPE	Victorized Clay Pipe	Concrete Pipe (non-reinforced)	Polyvinyl Chloride	POLYETHYLENE PIPE	Polyvinyl Chloride	SLIPLINED REINFORCED POLYESTER PIPE	CURED IN PLACE PIPE	SLIPLINED REINFORCED POLYESTER PIPE	CURED IN PLACE PIPE	SLIPLINED REINFORCED POLYESTER PIPE	CURED IN PLACE PIPE	Polyvinyl Chloride	SLIPLINED REINFORCED POLYESTER PIPE	SPHROLITE POLYETHYLENE PIPE	
Total	150	506	223	215	28,354	84	83,093	2,574	228,883	4,307	2,708	17,542	900	950	200	3,322	746	293	2,698	4,803	4,928	1,577	4,195	4,007	50	3,712	186	401,206
